

South Pine Street/Greer Street Phase 1

District(s): 03
 Project Manager: Chris Alonso
 Capital Project Officer: Sean Beauvais (210) 207-5836

Total Approved Budget

Source	Amount
2017 GO DRAINAGE IMPROVEMENT BOND	\$8,000,000
SAN ANTONIO WATER SYSTEM	\$1,358,702
CITY PUBLIC SERVICE	\$234,019
Total Fund	\$9,592,721

Cost Information

Category	Appropriations	Expenses To-date
Design	\$1,203,077	\$898,052
Right of Way	\$25,000	\$0
Environmental	\$193,940	\$35,355
Construction	\$8,141,904	\$6,007,970
PASA	\$28,800	\$28,800
Total	\$9,592,721	\$6,970,177

Project Status: COMPLETE
Consultant: Vickrey & Associates, Inc.
Contractor: E-Z Bel Construction, Ltd.
Estimated Construction Start: 10/2019
Estimated Construction Completion: 12/2020

Project Scope:

South Pine Street/Greer Street Phase 1 -- Construction of a storm drain system in Highland Park area to provide flooding relief to neighborhood streets and properties. This proposed phase includes curbs, sidewalks and driveway approaches as needed.

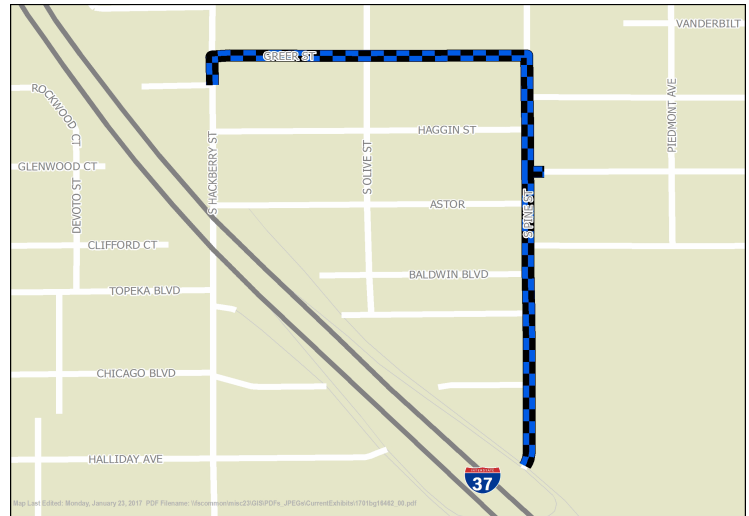


Fig. Last Edited: Monday, January 23, 2017 PDF Filename: \\sacmon\mca\2308\PDFs_JPEG\Curren\Exhibit\17916g16462_00.pdf
