

Thousand Oaks Drive (Wetmore Road to Perrin Beitel Road)

District(s): 10
 Project Manager: Chris Alonso
 Capital Project Officer: Cris Perez (210) 207-8154

Total Approved Budget

Source	Amount
2007 CERTIFICATES OF OBLIGATION	\$34,591
2008 CERTIFICATES OF OBLIGATION	\$250,176
2017 GO STREET IMPROVEMENT BOND	\$2,857,169
2010 CERTIFICATES OF OBLIGATION	\$121,214
SAN ANTONIO WATER SYSTEM	\$1,615,000
Total Fund	\$4,878,152

Cost Information

Category	Appropriations	Expenses To-date
Design	\$610,844	\$610,844
Environmental	\$66,299	\$66,299
Construction	\$4,190,208	\$4,190,208
PASA	\$10,800	\$10,800
Total	\$4,878,152	\$4,878,152

Project Status: COMPLETE
Consultant: Jones & Carter, Inc.
Contractor: E-Z Bel Construction, Ltd.
Estimated Construction Start: 04/2020
Estimated Construction Completion: 06/2021

Project Scope:

Thousand Oaks Drive (Wetmore Road to Perrin Beitel Road) -- Reconstruct outside lanes along Thousand Oaks from Wetmore to Perrin Beitel. Includes complete pavement improvements as appropriate and within available funding.

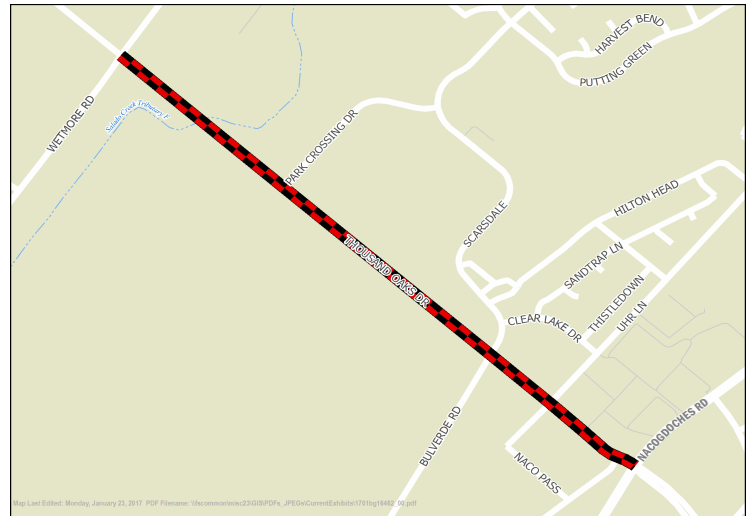


Fig. Last Edited: Monday, January 23, 2017 PDF Filename: \\common\ms\2308\PDFs_JPEG\Cover\Exhibit\7911g1442_01.pdf
