Project Number: 23-01560 **10/14/2026 5:49:18PM**

Bitters Road Intersection & Sidewalks (Savannah Pass to Blanco Road)

District(s): 09
Project Manager: Sean Strong
Capital Project Officer: James Hall (210) 207-6473

Total Approved Budget

Source	Amount
2017 GO STREET IMPROVEMENT BOND	$4,820,070
SAN ANTONIO WATER SYSTEM	$27,150
Total Fund	$4,847,220

Cost Information

Category	Appropriations	Expenses To-date
Design	$859,352	$859,352
Right of Way	$80,151	$80,151
Environmental	$65,794	$65,794
Construction	$4,198,676	$4,198,676
PASA	$22,860	$22,860
Total	$5,226,834	$5,226,834

Project Status: COMPLETE
Consultant: Garcia & Wright Consulting Engr.
Contractor: All In Construction, LLC

Estimated Construction Start: 10/2020
Estimated Construction Completion: 03/2022

Project Scope:
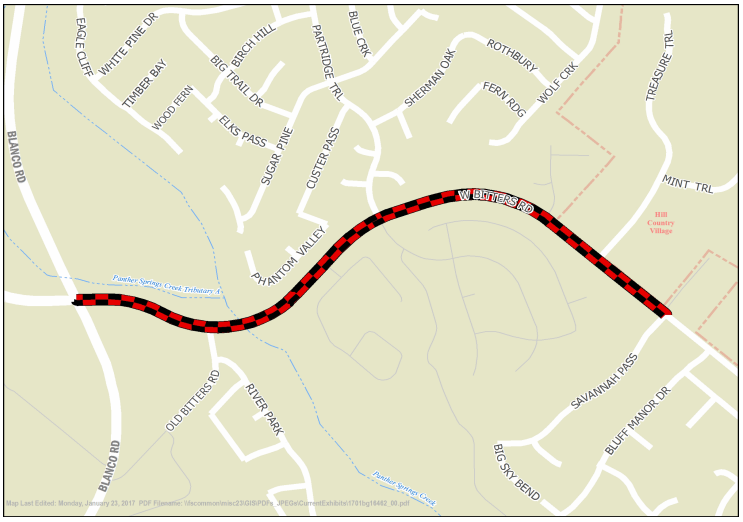
Bitters Rd Intersection & Sidewalks (Savannah Pass to Blanco Road) -- This project provides funding to construct an intersection, traffic signal and sidewalk improvements. Includes adding left-turn lanes at Savannah Pass and Partridge Trail; and a dedicated right-turn lane from Bitters onto northbound Blanco Road.
