Project Number: 23-01589 **4/18/20247:47:42PM**

Ingram Road (Potranco Road to Dead End)

District(s): 06
Project Manager: Chris Alonso
Capital Project Officer: Cris Perez (210) 207-8154

Total Approved Budget

Source	Amount
2017 GO STREET IMPROVEMENT BOND	$820,837
SAN ANTONIO WATER SYSTEM	$4,170
Total Fund	$825,007

Cost Information

Category	Appropriations	Expenses To-date
Design	$348,225	$348,225
Environmental	$4,170	$4,170
Construction	$471,782	$471,782
PASA	$829	$829
Total	$825,007	$825,007

Project Status: COMPLETE
Consultant: Developer (KFW Engineers)
Contractor: E-Z Bel Construction, Ltd.

Estimated Construction Start: 08/2019
Estimated Construction Completion: 09/2020

Project Scope:
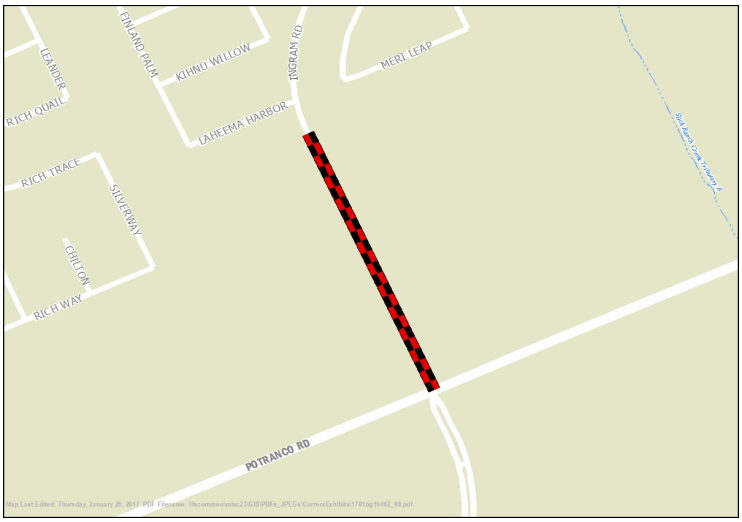
Ingram Road (Potranco Road to Dead End) -- Construct road extension from Potranco to Ingram dead end. Includes curbs, sidewalks, bike facilities and drainage improvements as appropriate and within available funding.
