Project Number: 23-01609 **10/14/2026 6:29:50PM**

South Alamo (Market Street to East César E. Chávez Boulevard)

District(s): City Wide, 01
Project Manager: Kathryn Otto
Capital Project Officer: Joe Doctor (210) 207-8415

Total Approved Budget

Source	Amount
TREE PRESERVATION FUND	$750,000
2017 GO STREET IMPROVEMENT BOND	$20,561,541
2022 CERTIFICATES OF OBLIGATION	$8,000,000
2025 CERTIFICATES OF OBLIGATION	$7,500,000
2026 CERTIFICATES OF OBLIGATION	$2,566,805
SAN ANTONIO WATER SYSTEM	$16,040,081
CITY PUBLIC SERVICE	$3,531,705
Total Fund	$58,950,133

Cost Information

Category	Appropriations	Expenses To-date
Design	$2,355,194	$2,341,814
Right of Way	$49	$49
Environmental	$2,550,828	$1,178,733
Construction	$54,003,561	$44,600,494
PASA	$40,500	$40,500
Total	$58,950,133	$48,161,591

Project Status: COMPLETE
Consultant: Sundt Construction Inc
Contractor:

Estimated Construction Start: 12/2022
Estimated Construction Completion: 04/2026

Project Scope:
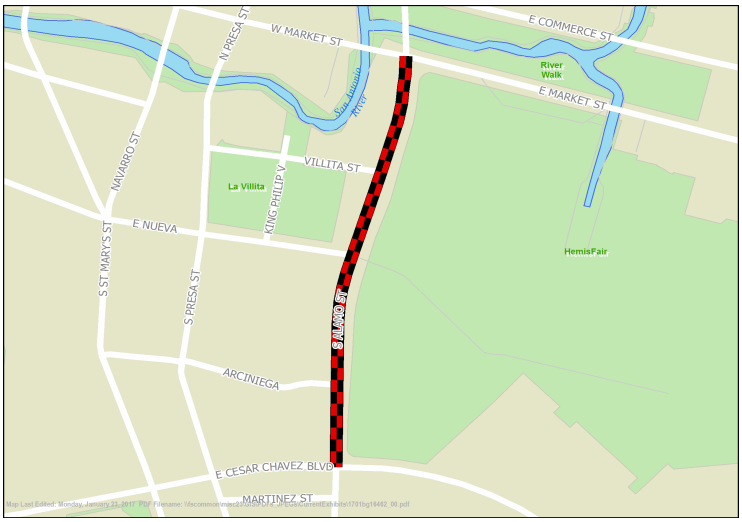
South Alamo (Market Street to East César E. Chávez Boulevard) -- Reconstruct Alamo St. from Market to César E. Chávez. Includes pedestrian amenities and enhancements as appropriate and within available funding.
