Project Number: 23-01610 **4/25/2024 4:41:23PM**

South Presa Street (Southeast Military Drive to Southcross Boulevard)

District(s): City Wide
Project Manager: Kathryn Otto
Capital Project Officer: James Hall (210) 207-6473

Total Approved Budget

Source	Amount
2012 GO STREET IMPROVEMENT BOND	$2,000,000
2017 GO STREET IMPROVEMENT BOND	$6,675,400
TEXAS DEPARTMENT OF TRANSPORTATION	$8,712,000
SAN ANTONIO WATER SYSTEM	$2,805,052
CITY PUBLIC SERVICE	$2,012,771
Total Fund	$22,205,223

Cost Information

Category	Appropriations	Expenses To-date
Design	$2,334,151	$2,209,513
Right of Way	$48,915	$48,915
Environmental	$648,373	$310,750
Construction	$19,155,783	$15,699,659
PASA	$18,000	$18,000
Total	$22,205,223	$18,286,838

Project Status: UNDER CONSTRUCTION
Consultant: RPS Klotz Associates
Contractor:

Estimated Construction Start: 09/2022
Estimated Construction Completion: 04/2024

Project Scope:
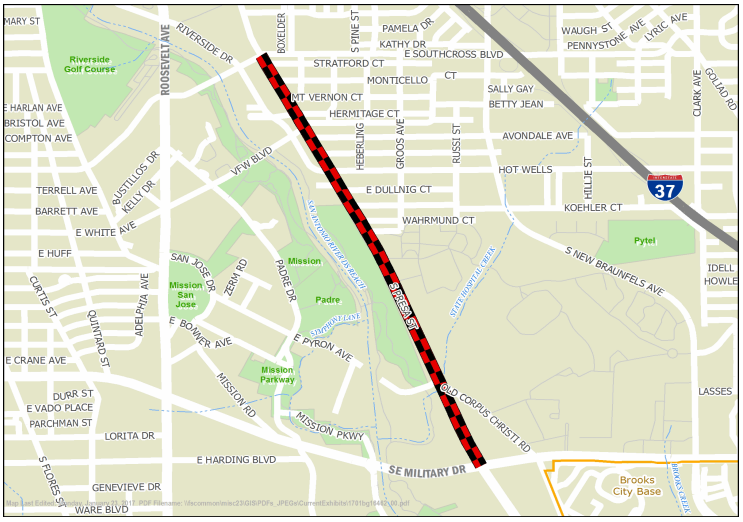
South Presa Street (Southeast Military Drive to Southcross Boulevard) -- Construct corridor improvements from Military to Southcross. Includes pedestrian amenities and enhancements as appropriate and within available funding.
