Project Number: 23-01634 **10/14/2026 5:48:58PM**

San Pedro Creek

District(s): City Wide
Project Manager: Sean Reich
Capital Project Officer: Joe Doctor (210) 207-8415

Total Approved Budget

Source	Amount
2017 GO DRAINAGE IMPROVEMENT BOND	$14,599,999
Total Fund	$14,599,999

Cost Information

Category	Appropriations	Expenses To-date
Design	$12,008	$12,008
Construction	$14,570,471	$14,570,471
PASA	$17,520	$17,520
Total	$14,599,999	$14,599,999

Project Status: COMPLETE
Consultant: San Antonio River Authority
Contractor: Sundt Davila

Estimated Construction Start: 05/2018
Estimated Construction Completion: 03/2022

Project Scope:
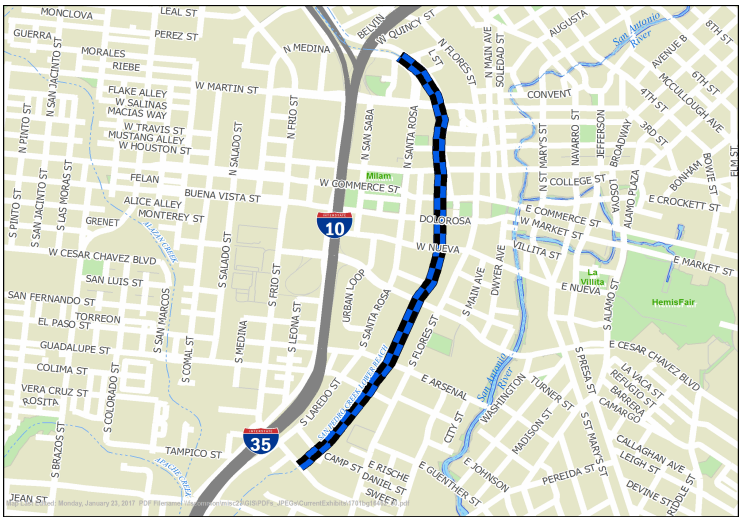
San Pedro Creek -- Leverage local funding to support a improvements associated with the drainage components of Phase 1 and 2 of the San Pedro Creek Restoration Project.
