Project Number: 23-01665 **4/19/2024 3:16:20PM**

Gilbert Morgan Denman, Jr. Park

District(s): 08
Project Manager: Sean Duncan
Capital Project Officer:

Total Approved Budget

Source	Amount
2017 GO PARKS IMPROVEMENT BOND	$400,000
Total Fund	$400,000

Cost Information

Category	Appropriations	Expenses To-date
Design	$103,664	$103,362
Environmental	$2,572	$2,572
Construction	$291,963	$292,265
PASA	$1,800	$1,800
Total	$400,000	$400,000

Project Status: COMPLETE
Consultant: Westeast Design Group, LLC
Contractor: ALP Contracting

Estimated Construction Start: 08/2019
Estimated Construction Completion: 05/2020
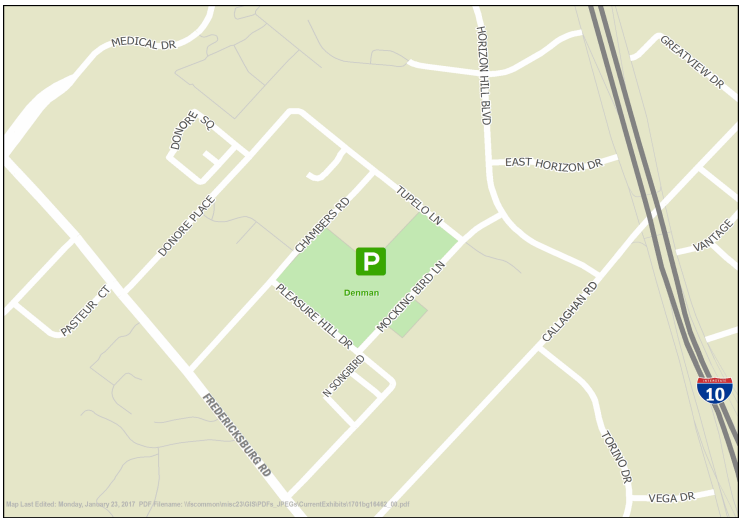
Project Scope:
Gilbert Morgan Denman, Jr. Park -- General park improvements and rehabilitation which may include trail enhancements and restroom development.
