Project Number: 23-01718 **10/14/2026 5:48:59PM**

Zoo Parking Garage

District(s): City Wide, 01
Project Manager: MARK BEAVERS
Capital Project Officer:

Total Approved Budget

Source	Amount
2017 GO PARKS IMPROVEMENT BOND	$11,750,000
PARKING OPERATING AND MAINTENANCE FUND	$558,456
Total Fund	$12,308,456

Cost Information

Category	Appropriations	Expenses To-date
Design	$209,466	$209,466
Environmental	$36,794	$36,794
Construction	$12,037,560	$12,037,560
Other	$9,518	$9,518
PASA	$35,250	$35,250
Total	$12,328,590	$12,328,590

Project Status: COMPLETE
Consultant: Alamo Architects
Contractor: Guido Brothers Construction

Estimated Construction Start: 11/2018
Estimated Construction Completion: 10/2019
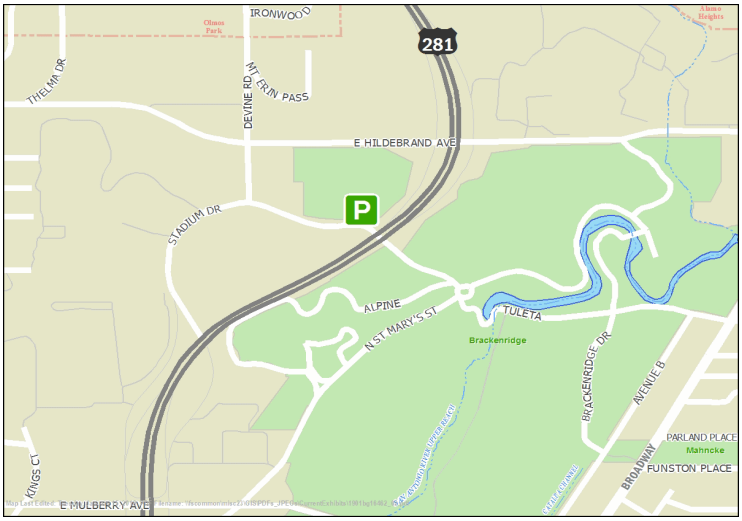
Project Scope:
Zoo Parking Garage -- Development of a new parking garage facility to service Brackenridge Park and San Antonio Zoo patrons.
