Project Number: 23-01729 **10/14/2026 6:29:54PM**

The Neighborhood Place Cultural/Community Center

District(s): 05

Project Manager: Jeni O'Quinn

Capital Project Officer: Randy Matyear (210) 207-2155

Total Approved Budget

Source	Amount
2017 GO LIBRARY IMPROVEMENT BOND	$1,500,000
Total Fund	$1,500,000

Cost Information

Category	Appropriations	Expenses To-date
Design	$10,897	$10,897
Construction	$1,487,602	$1,487,602
PASA	$1,500	$1,500
Total	$1,500,000	$1,500,000

Project Status: COMPLETE

Consultant: Piwonka Sturrock Architects, LLC

Contractor: PSE Contracting

Estimated Construction Start: 12/2017

Estimated Construction Completion: 07/2019

Project Scope:
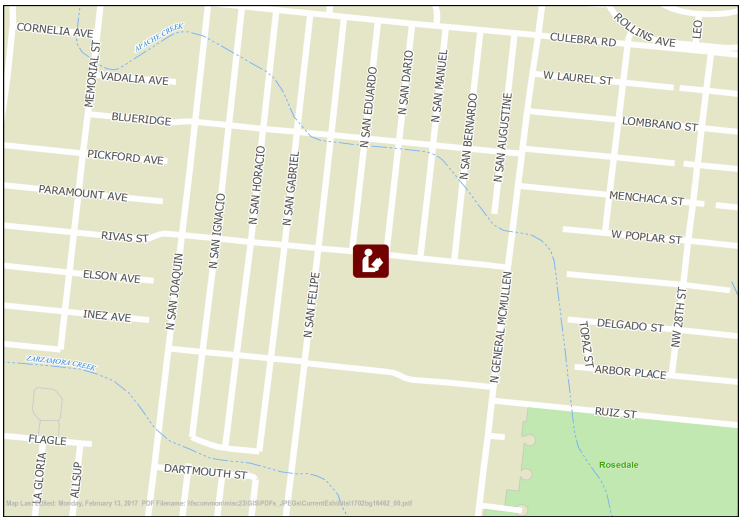
The Neighborhood Place Cultural/Community Center -- Leverage funding for facility improvements to potentially include gym, parking lot, cafeteria and kitchen.
